AUTOMOTIVE PRODUCTION LINE EXPANSION

SCHEDULE & PROGRESS



Data Date
30 Sep 2026


18 May 2027
Planned_Finish_Display

30 Sep 2026
Data_Date_Display 1


49
Total_Activities

6.63%
Average_Progress_Pct

ACTIVITY STATUS

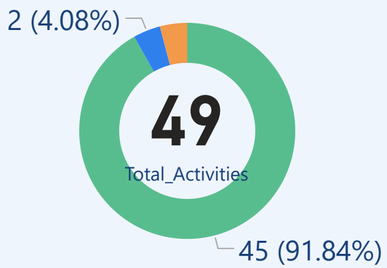

ACTIVITY PROGRESS

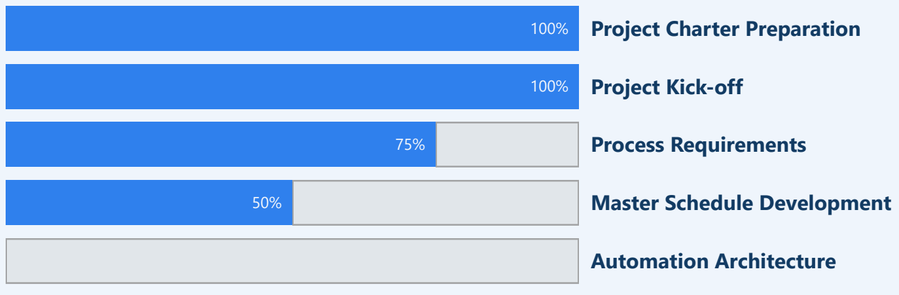

SCHEDULE HEALTH


- Baseline Set
- Status Date Set
- Progress Updated
- MSP Schedule Aligned

Project Schedule is on track

ACTIVITY DETAILS

Activity ID	Task Name	Status	% Complete	Start	Finish	Sum of Budget Cost (USD)	Sum of Actual Cost (
A1230	Automation Architecture	Not Started	0.00	46324	46333	47400	
A1330	Contract Negotiation	Not Started	0.00	46363	46370	58200	
A1530	Conveyor Installation	Not Started	0.00	46412	46419	47400	
A1390	Conveyor Manufacturing	Not Started	0.00	46370	46394	85600	
A1040	Cost Baseline Development	Not Started	0.00	46321	46326	50600	
A1660	Cycle Time Measurement	Not Started	0.00	46476	46481	46400	
A1270	Design Approval	Not Started	0.00	46337	46340	55400	
A1630	Dry Run	Not Started	0.00	46461	46466	59000	
A1210	Electrical Design	Not Started	0.00	46324	46335	42500	
A1460	Equipment Delivery & Inspection	Not Started	0.00	46401	46406	47000	
A1160	Equipment Specifications	Not Started	0.00	46317	46324	45600	
A1720	Final Performance Verification	Not Started	0.00	46512	46519	59000	
A1490	Foundation Preparation	Not Started	0.00	46350	46357	39000	
Total			**6.63**			**2622300**	**12**

BUDGET VS ACTUAL COST BY WBS

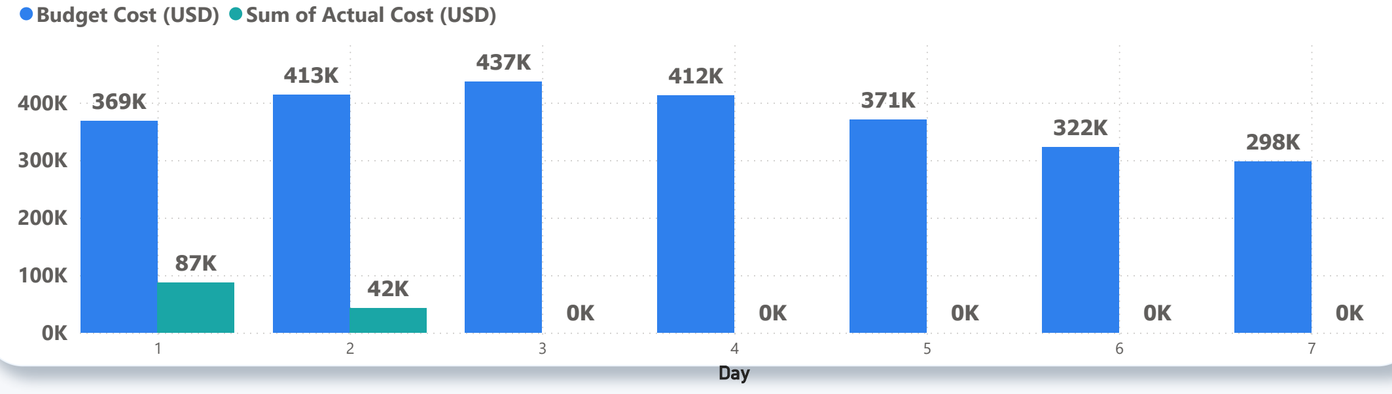

PROJECT COST & EVM DASHBOARD

AUTOMOTIVE PRODUCTION LINE EXPANSION



Data Date
30 Sep 2026


2.62M
BAC

445K
AC_Total


0.96
CPI_Value

792K
PV_Total

AC, PV & SV BY WEEK ENDING

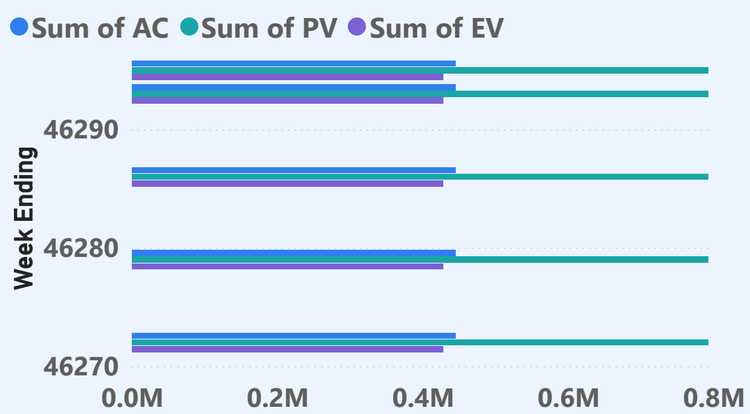

CV BY WEEK ENDING

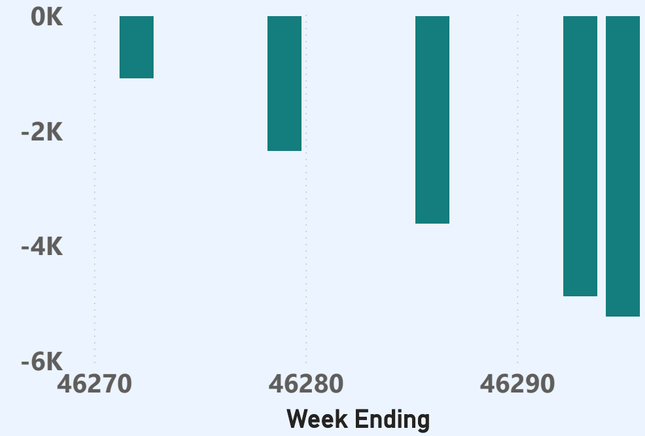

COST % EVM

427,828
EV_Total

0.54
SPI_Value

2.73M
EAC

-104.9K
VAC

TOTALS

792.05K
PV_Total


427.83K
EV_Total

2.73M
EAC


-104.89K
VAC

AUTOMOTIVE PRODUCTION LINE EXPANSION

COST & EVM TREND

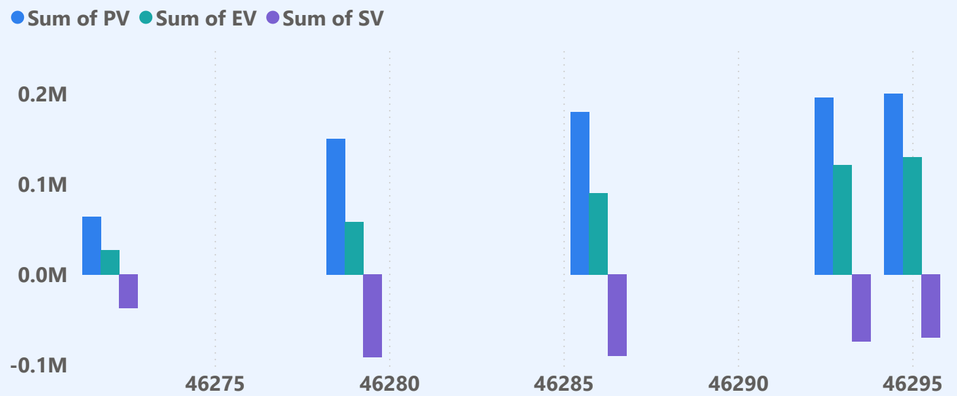

CPI PERFORMANCE

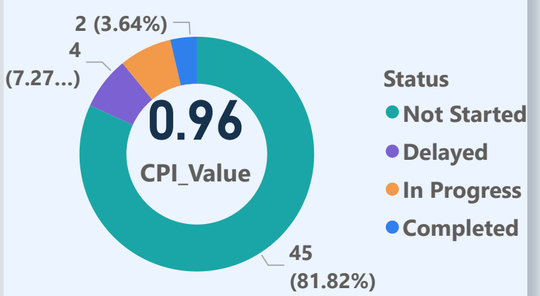

AUTOMOTIVE PRODUCTION LINE EXPANSION

RISK DASHBOARD




Data Date
30 Sep 2026

Total_Risks	High_Risks	Medium_Risks	Low_Risks	Average_Risk_Score
6	3	3	0	13.83


Count of Risk ID by Category



Count of Risk ID by Status

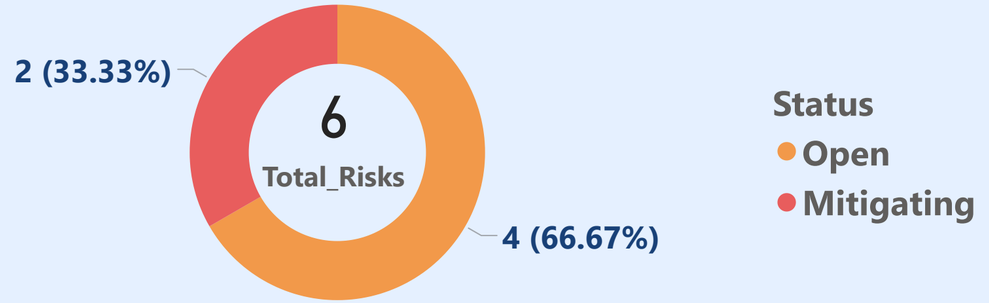

Sum of Score by Risk ID

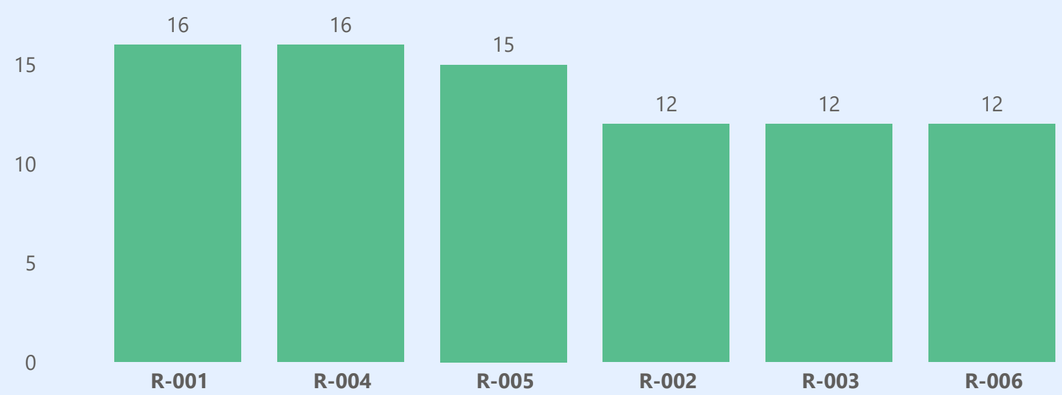

Risk Register

Risk ID	Category	Risk Description	Probability	Impact	Score	Status	Mitig
R-003	Civil & Site	Utility modification delay	4	3	12	Open	Confirm utility readine
R-002	Engineering	Late design approval	3	4	12	Mitigating	Early review workshop
R-001	Procurement	Robot cell delivery delay	4	4	16	Open	Expedite supplier mile
R-004	Automation	PLC/MES integration issue	4	4	16	Open	Interface test plan anc
R-006	Production Ramp-up	High initial defect rate	3	4	12	Open	Pilot quality controls a
R-005	Testing	Performance test failure	3	5	15	Mitigating	Pre-test checklist and

AUTOMOTIVE PRODUCTION LINE EXPANSION

PROJECT CONTROLS — EXECUTIVE OVERVIEW

Data Date: 30 Sep 2026

BAC
Budget at Completion
2.62M

Planned Value (PV)
Value of Work Scheduled
792.05K

Earned Value (EV)
Value of Work Performed
427.83K

Actual Cost (AC)
Actual Cost Incurred
444.9K

Cost Variance (CV)
EV – AC
-17.11K


Schedule Variance (SV)
EV – PV
-364.22K

Cost Performance Index (CPI)
EV / AC
0.96

Schedule Performance Index (SPI)
EV / PV
0.54

WEEKLY EVM PERFORMANCE

PV (Planned Value) EV (Earned Value) AC (Actual Cost)

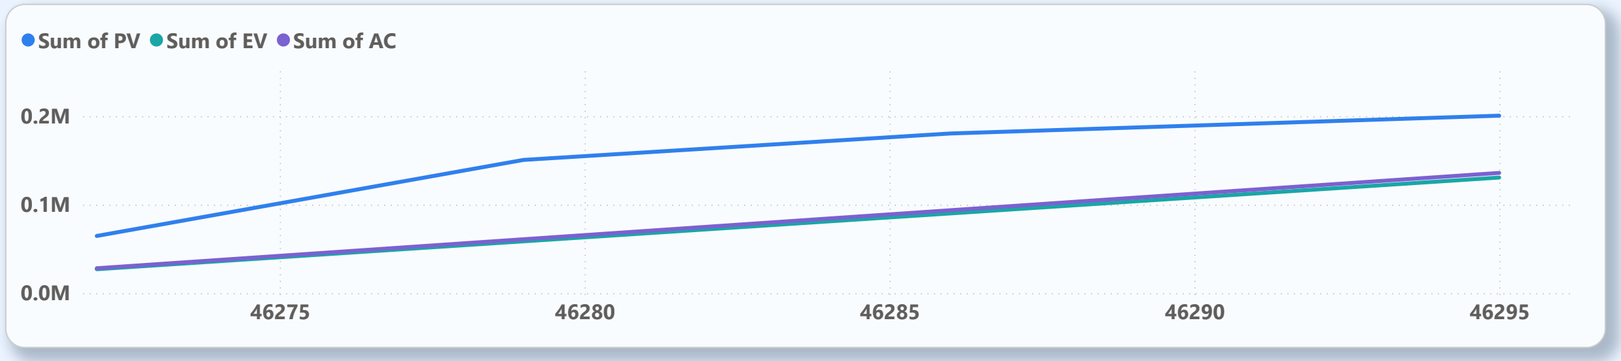


PROJECT STATUS
On Track


CPI 0.96 | SPI 0.54

Cost and schedule performance requires monitoring.

WEEKLY PROJECT PROGRESS

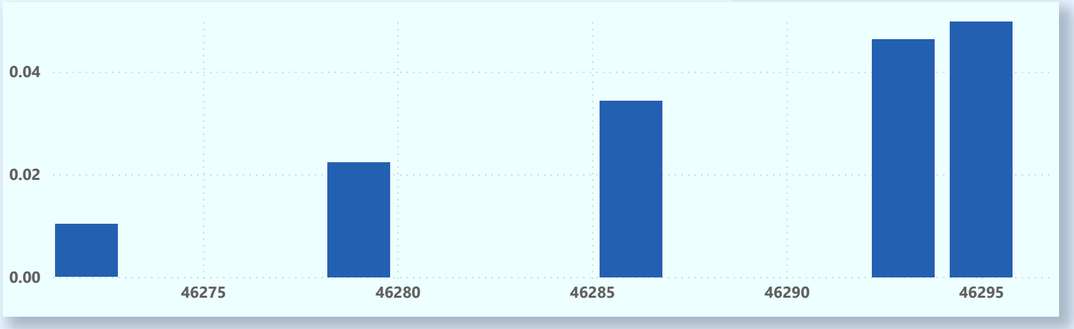

RISK STATUS

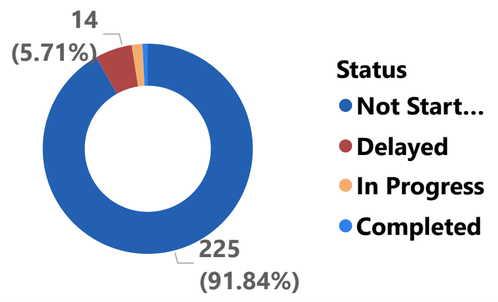

KEY FOCUS

- ✓ Monitor critical risk
- ✓ Control cost variance
- ✓ Improve schedule performance
- ✓ Maintain project control
